




## Node Inspection - 3/07/2019 - SMH.08532432

Date of inspection Node name		Node type	Town	Location/Street	No.
3/07/2019	SMH.08532432	Sewer Maintenance Hole	Brisbane	34 Serenity DR	3.00
Name of operator	Precipitation	Pre-cleaned		Depth to Invert [m]	Job Number
Hugh	No precipitation	Yes		3.53	1

Node material	Concrete segments	Shape of Circ	cular Width o	1050.00		
General comment	Sewer				1	<u> </u>



Observations							
Nr.	Depth [m] Code Observation			Remarks			
1	0.02	HSTAC	Start feature, access cover.				
2							
3	2.94	HCNDC	A conduit or ventilation pipe has been connected to the maintenance structure, drop chamber.				
4	3.19	HSLLCM	Ladder support missing (Ladder clip missing).				
6	3.49	HCPCI	A conduit connecting to the maintenance structure, circular, incoming. at 1 o'clock				
5	3.52	HCPCO	A conduit connecting to the maintenance structure, circular, outgoing. at 9 o'clock				

## Entries (In-Outlets)

No.	Direction	Drop [m]	Clock Position	Shape	Material	Diameter 1 [mm]	Diameter 2 [mm]	Remarks
1	In	3.49	6	Circular		150		
2	Out	3.52	12	Circular		150		

1

Page 1



## Node Pictures - 3/07/2019 - SMH.08532432

Date of inspection Node name Town Location/Street Name of operator 3/07/2019 SMH.08532432 Brisbane 34 Serenity DR Hugh



1, , 0.47 Ladder support missing (Ladder clip missing).



2, , 0.47 Ladder support missing (Ladder clip missing).



 $\mathbf{3},\,,\,\mathbf{3.19}$  Ladder support missing (Ladder clip missing).




 $\mathbf{4},\ , \ 3.49$  A conduit connecting to the maintenance structure, circular, incoming. at 1 o'clock



## Clever Scan - 3/07/2019 - SMH.08532432

No.	Node name	Alternative ID	Client's Job Ref	Contractor's Job Ref
3	SMH 08532432			

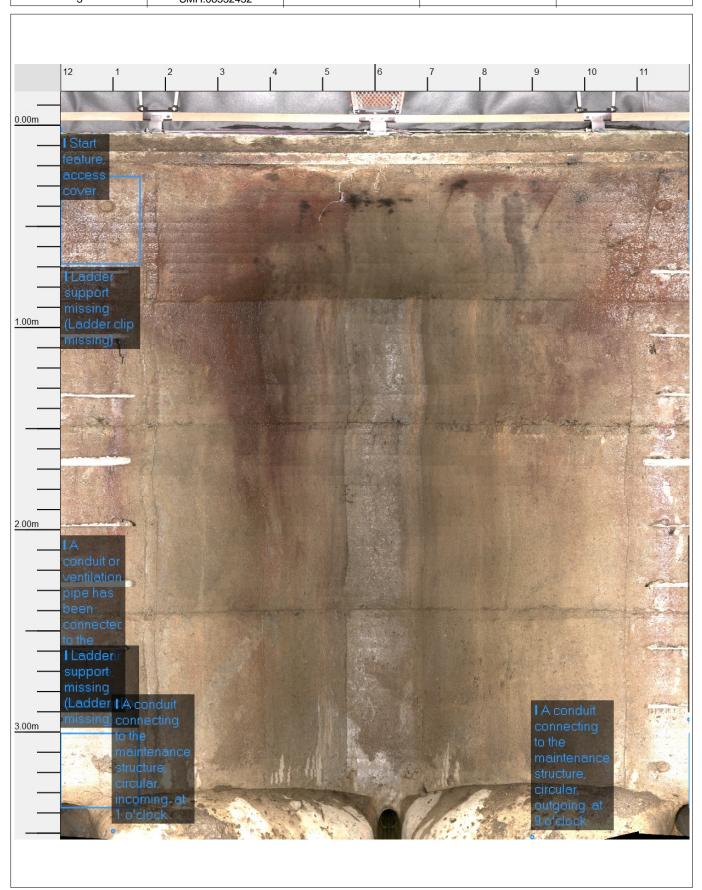

CleverScan Demo Light 3
